

Allegan Downtown Streetscape Project

Date: July 14, 2023

Current Progress

The old seawalls have been passed through as sanitary sewer work continued forward along the Riverfront Plaza this week and began making its way up the slope to Hubbard St. Higher up in downtown, sidewalk removals began in force on Brady St to make way for new conduit and sidewalk, bringing the beginning surface touches of the streetscape into view. Once again, as concrete work and excavations are performed at various locations in the downtown area, please refrain from disturbing these areas so that concrete can cure properly without disfiguration.

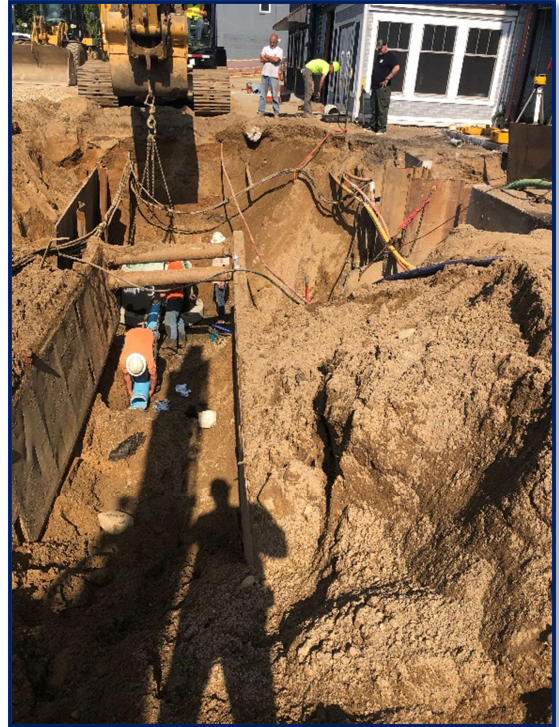


Fig 1: Milbocker lays sanitary sewer line along Riverfront Plaza.



Fig 2: New sanitary sewer manholes are installed on Riverfront Plaza

Upcoming Work

This coming week, the Riverfront sanitary sewer will be wrapped up and taken up the hill to Hubbard St. Following this work, sanitary will progress westward along Hubbard as conduit and lighting are placed on Brady and then Hubbard St. Once these utilities are placed, sidewalk will be poured as the downtown continues to be rejuvenated.

Throughout the project's duration, the contractor remains committed to minimizing disruptions and maintaining accessibility for residents and businesses. Sidewalks will be preserved as long as possible to ensure continued access. However, now that existing sidewalks are being actively removed, the affected property owners will be contacted in advance, and temporary walkways will be established as necessary.
