


## Allegan Downtown Streetscape Project

Date: November 17, 2023

### Current Progress


Restoration and landscaping activities have continued this week with work complete on East Hubbard, West Hubbard, and Locust Streets as well as Riverfront Plaza. Crews from Twin Lakes Nursery will continue, as conditions allow, to place trees and plants along Brady and State Streets.

Milbocker is continuing road building activities with the top course paving complete on all streets. Along with newly placed brick pavers, crews will be working on installing lighting, pavement markings, and finishing work on the seat walls located throughout the site. As with freshly placed concrete, please remember to be on the lookout for and to respect signs and barriers to protect these areas until they are ready to be open to traffic.

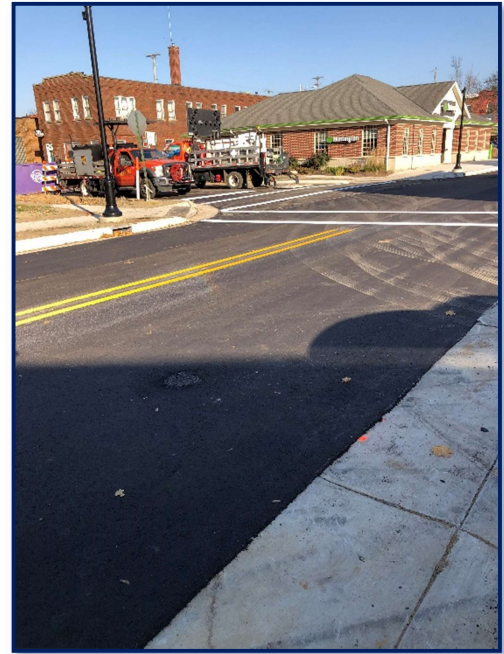

*Figure 1: PK Contracting begins to paint pavement markings onto various streets within the project limits.*

### Upcoming Work

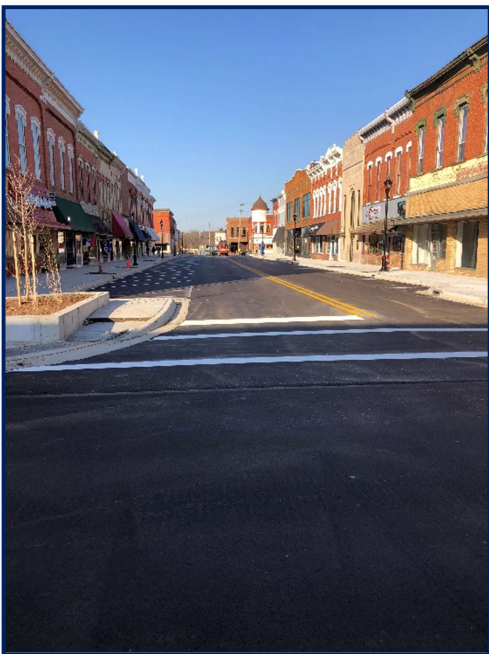

*Figure 2: Locust Street once more begins to take shape after receiving top course asphalt and permanent pavement markings.*

Road building activity will be wrapping up with significant work transitioning to pedestrian areas. This is expected to include finishing veneer and capping work on seat walls, wiring and lighting installation, brick paver placement, and signage installation.

Throughout the project's duration, the contractor remains committed to minimizing disruptions and maintaining accessibility for residents and businesses. As existing sidewalks are being replaced, there will be temporary closures. Affected property owners will be contacted in advance and temporary walkways will be established as necessary.

Please be on the lookout for freshly placed concrete. Signs and caution tape are placed to help identify these areas. If you step in wet concrete, please notify Abonmarche Staff or the crew members while a repair is possible. The project team wants to deliver a first-class finished product in a timely manner.
