

Allegan Downtown Streetscape Project

Date: September 1, 2023

Current Progress

Milbocker & Sons continue to work throughout the downtown area as underground utilities get closer to completion and more surface components are built. In fact, the week started with the paving of base course asphalt along Brady St and on Hubbard St east of Locust St. While not open to the public yet, this brings these roads one course of asphalt closer to being drivable and also helps control dust and sedimentation coming from the aggregate base under these roadways.

With paving occurring in the southeastern portion of the project limits, Milbocker's crews continued to install water services on Locust St and adjusted roadway grades on Hubbard St to prepare for new curbs and sidewalk. This grading will allow for Duran Concrete to come back and pour these items so that surface work can continue on Hubbard St.

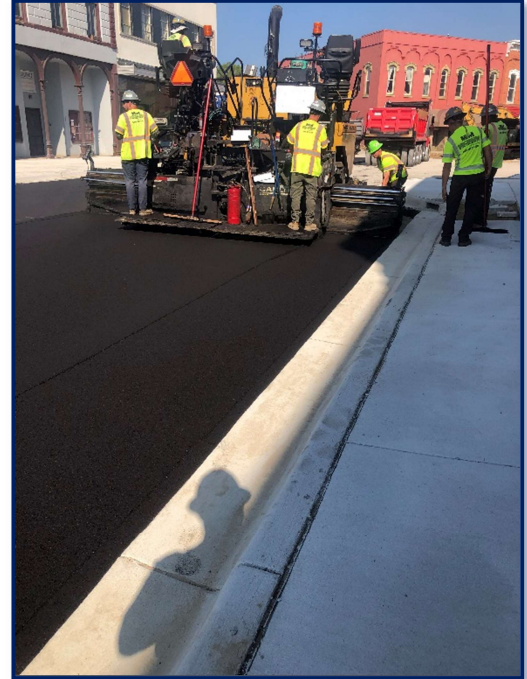


Fig 1: Michigan Paving paves the base course of asphalt along Brady St



Fig 2: Milbocker continues to replace water services along Locust St

Upcoming Work

Underground utilities get closer to being completed each week as Milbocker's crew plans to lay storm and sanitary sewer next week on Locust and Trowbridge St. This work will finish a main component of the underground work in this area, with the structural abandonment of some underground areas occurring right afterward. As this work takes place, Duran Concrete will also be working on pouring more sidewalks along Brady and Hubbard St.

Throughout the project's duration, the contractor remains committed to minimizing disruptions and maintaining accessibility for residents and businesses. Sidewalks will be preserved as long as possible to ensure continued access. However, now that existing sidewalks are being actively removed, the affected property owners will be contacted in advance, and temporary walkways will be established as necessary. Please refrain from disturbing these pours so that concrete can cure properly without disfiguration.
